

BlueCuda Entity Relationship Diagram

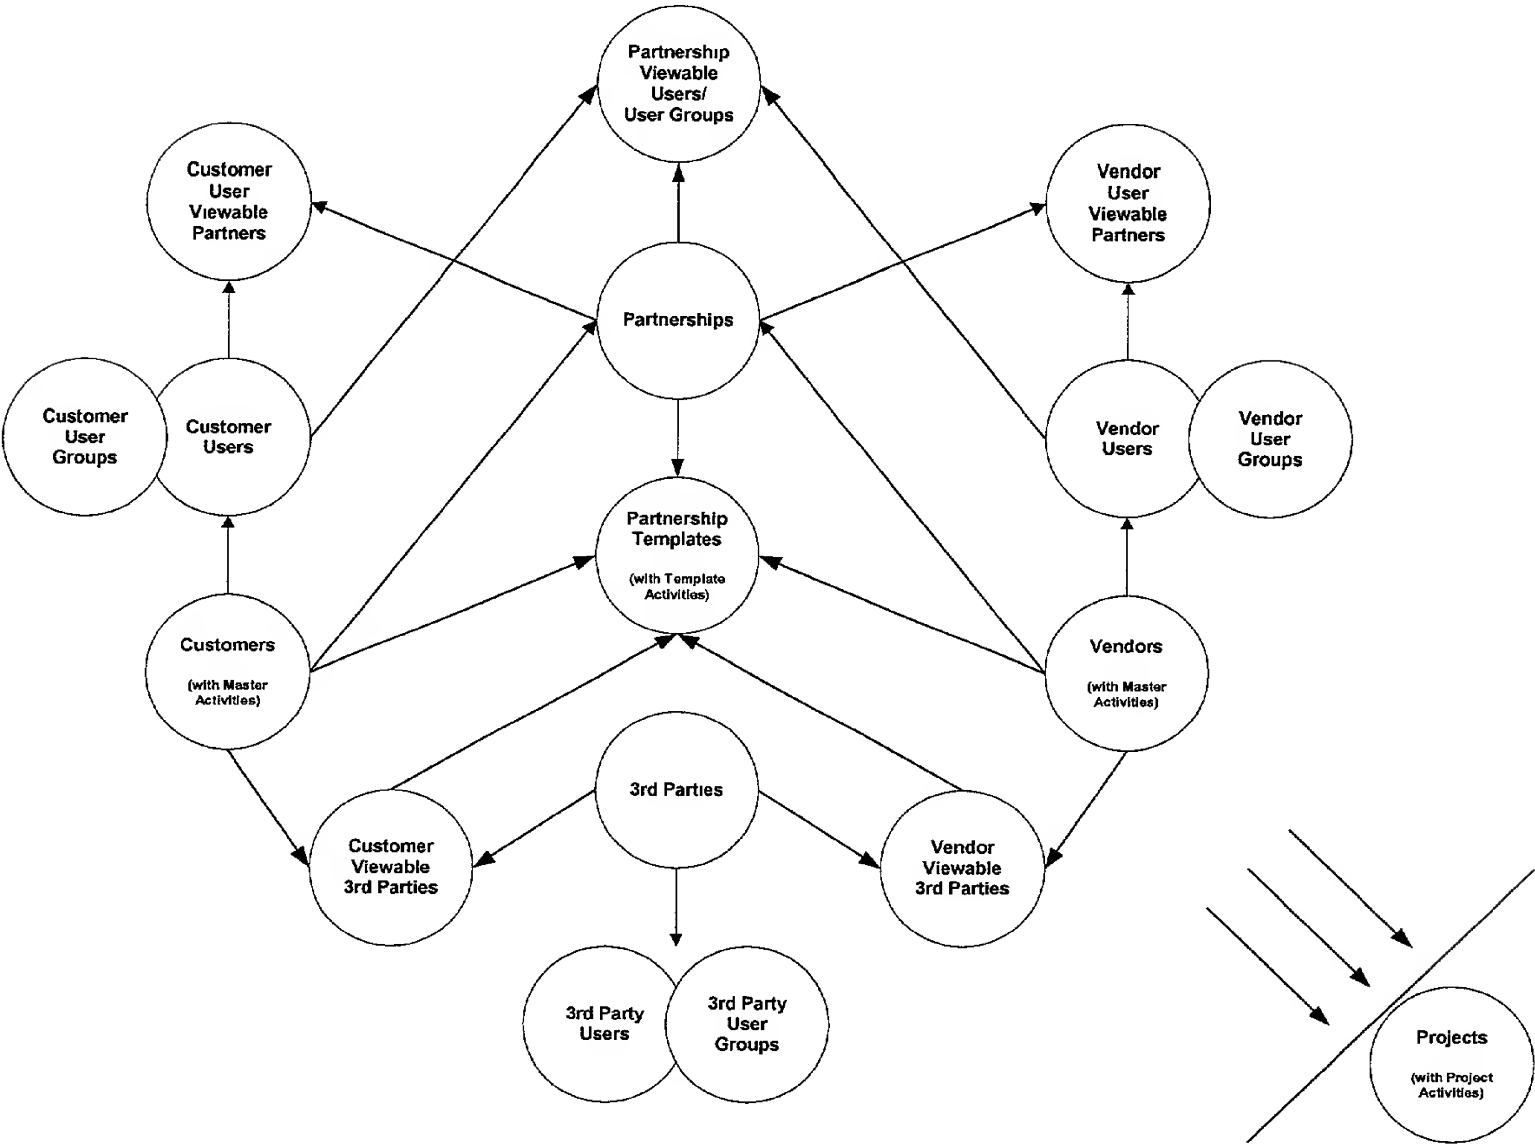


FIGURE 1

09966710-092601
00260-0129660




Company Profile	
<div>SubmitCancel</div>	
Name:	ABC Packaging Company
Division:	Display Division
Workdays:	<input type="checkbox"/> Sun <input checked="" type="checkbox"/> Mon <input checked="" type="checkbox"/> Tue <input checked="" type="checkbox"/> Wed <input checked="" type="checkbox"/> Thu <input checked="" type="checkbox"/> Fri <input type="checkbox"/> Sat
Non-Working Dates:	<div><div></div><div>12/24/2001, 12/25/2001</div><div> </div></div>

FIGURE 2

Activities	Workdays
Seq	Activity Name
1	Cost & Feasibility Form Initiated
2	Brand Approvals
3	Submit Design Development Request to Vendors
4	Structure Submitted to Customer
5	Structure Approved
6	Die-Lines Submitted to Art Agency
7	Art Submitted to Customer by Agency
8	Art Approved
9	Specs Submitted for Pricing
10	Pricing Submitted to Customer
11	Pricing Approved
12	Purchase Order Issued
13	Product Ordered
14	Work Order Submitted to Manufacturing
15	Cutting Dies Ordered
16	Printing Plates Ordered
17	Outside Parts Purchased
18	All Proofs Approved
19	Component Manufacturing Start
20	Component Manufacturing Finish
21	Components Received at Assembly
22	Product Received at Assembly
23	Assembly Start

FIGURE 2A

Activity Table More Fields							
Activities		Workdays					
Seq	Working Days						
1	<input type="checkbox"/> Sun	<input checked="" type="checkbox"/> Mon	<input checked="" type="checkbox"/> Tue	<input checked="" type="checkbox"/> Wed	<input checked="" type="checkbox"/> Thu	<input checked="" type="checkbox"/> Fri	<input type="checkbox"/> Sat
2	<input type="checkbox"/> Sun	<input checked="" type="checkbox"/> Mon	<input checked="" type="checkbox"/> Tue	<input checked="" type="checkbox"/> Wed	<input checked="" type="checkbox"/> Thu	<input checked="" type="checkbox"/> Fri	<input type="checkbox"/> Sat
3	<input type="checkbox"/> Sun	<input checked="" type="checkbox"/> Mon	<input checked="" type="checkbox"/> Tue	<input checked="" type="checkbox"/> Wed	<input checked="" type="checkbox"/> Thu	<input checked="" type="checkbox"/> Fri	<input type="checkbox"/> Sat
4	<input type="checkbox"/> Sun	<input checked="" type="checkbox"/> Mon	<input checked="" type="checkbox"/> Tue	<input checked="" type="checkbox"/> Wed	<input checked="" type="checkbox"/> Thu	<input checked="" type="checkbox"/> Fri	<input type="checkbox"/> Sat
5	<input type="checkbox"/> Sun	<input checked="" type="checkbox"/> Mon	<input checked="" type="checkbox"/> Tue	<input checked="" type="checkbox"/> Wed	<input checked="" type="checkbox"/> Thu	<input checked="" type="checkbox"/> Fri	<input type="checkbox"/> Sat
6	<input type="checkbox"/> Sun	<input checked="" type="checkbox"/> Mon	<input checked="" type="checkbox"/> Tue	<input checked="" type="checkbox"/> Wed	<input checked="" type="checkbox"/> Thu	<input checked="" type="checkbox"/> Fri	<input type="checkbox"/> Sat
7	<input type="checkbox"/> Sun	<input checked="" type="checkbox"/> Mon	<input checked="" type="checkbox"/> Tue	<input checked="" type="checkbox"/> Wed	<input checked="" type="checkbox"/> Thu	<input checked="" type="checkbox"/> Fri	<input type="checkbox"/> Sat
8	<input type="checkbox"/> Sun	<input checked="" type="checkbox"/> Mon	<input checked="" type="checkbox"/> Tue	<input checked="" type="checkbox"/> Wed	<input checked="" type="checkbox"/> Thu	<input checked="" type="checkbox"/> Fri	<input type="checkbox"/> Sat
9	<input type="checkbox"/> Sun	<input checked="" type="checkbox"/> Mon	<input checked="" type="checkbox"/> Tue	<input checked="" type="checkbox"/> Wed	<input checked="" type="checkbox"/> Thu	<input checked="" type="checkbox"/> Fri	<input type="checkbox"/> Sat
10	<input type="checkbox"/> Sun	<input checked="" type="checkbox"/> Mon	<input checked="" type="checkbox"/> Tue	<input checked="" type="checkbox"/> Wed	<input checked="" type="checkbox"/> Thu	<input checked="" type="checkbox"/> Fri	<input type="checkbox"/> Sat
11	<input type="checkbox"/> Sun	<input checked="" type="checkbox"/> Mon	<input checked="" type="checkbox"/> Tue	<input checked="" type="checkbox"/> Wed	<input checked="" type="checkbox"/> Thu	<input checked="" type="checkbox"/> Fri	<input type="checkbox"/> Sat
12	<input type="checkbox"/> Sun	<input checked="" type="checkbox"/> Mon	<input checked="" type="checkbox"/> Tue	<input checked="" type="checkbox"/> Wed	<input checked="" type="checkbox"/> Thu	<input checked="" type="checkbox"/> Fri	<input type="checkbox"/> Sat
13	<input type="checkbox"/> Sun	<input checked="" type="checkbox"/> Mon	<input checked="" type="checkbox"/> Tue	<input checked="" type="checkbox"/> Wed	<input checked="" type="checkbox"/> Thu	<input checked="" type="checkbox"/> Fri	<input type="checkbox"/> Sat
14	<input type="checkbox"/> Sun	<input checked="" type="checkbox"/> Mon	<input checked="" type="checkbox"/> Tue	<input checked="" type="checkbox"/> Wed	<input checked="" type="checkbox"/> Thu	<input checked="" type="checkbox"/> Fri	<input type="checkbox"/> Sat
15	<input type="checkbox"/> Sun	<input checked="" type="checkbox"/> Mon	<input checked="" type="checkbox"/> Tue	<input checked="" type="checkbox"/> Wed	<input checked="" type="checkbox"/> Thu	<input checked="" type="checkbox"/> Fri	<input type="checkbox"/> Sat
16	<input type="checkbox"/> Sun	<input checked="" type="checkbox"/> Mon	<input checked="" type="checkbox"/> Tue	<input checked="" type="checkbox"/> Wed	<input checked="" type="checkbox"/> Thu	<input checked="" type="checkbox"/> Fri	<input type="checkbox"/> Sat
17	<input type="checkbox"/> Sun	<input checked="" type="checkbox"/> Mon	<input checked="" type="checkbox"/> Tue	<input checked="" type="checkbox"/> Wed	<input checked="" type="checkbox"/> Thu	<input checked="" type="checkbox"/> Fri	<input type="checkbox"/> Sat
18	<input type="checkbox"/> Sun	<input checked="" type="checkbox"/> Mon	<input checked="" type="checkbox"/> Tue	<input checked="" type="checkbox"/> Wed	<input checked="" type="checkbox"/> Thu	<input checked="" type="checkbox"/> Fri	<input type="checkbox"/> Sat
19	<input type="checkbox"/> Sun	<input checked="" type="checkbox"/> Mon	<input checked="" type="checkbox"/> Tue	<input checked="" type="checkbox"/> Wed	<input checked="" type="checkbox"/> Thu	<input checked="" type="checkbox"/> Fri	<input type="checkbox"/> Sat
20	<input type="checkbox"/> Sun	<input checked="" type="checkbox"/> Mon	<input checked="" type="checkbox"/> Tue	<input checked="" type="checkbox"/> Wed	<input checked="" type="checkbox"/> Thu	<input checked="" type="checkbox"/> Fri	<input type="checkbox"/> Sat
21	<input type="checkbox"/> Sun	<input checked="" type="checkbox"/> Mon	<input checked="" type="checkbox"/> Tue	<input checked="" type="checkbox"/> Wed	<input checked="" type="checkbox"/> Thu	<input checked="" type="checkbox"/> Fri	<input type="checkbox"/> Sat
22	<input type="checkbox"/> Sun	<input checked="" type="checkbox"/> Mon	<input checked="" type="checkbox"/> Tue	<input checked="" type="checkbox"/> Wed	<input checked="" type="checkbox"/> Thu	<input checked="" type="checkbox"/> Fri	<input type="checkbox"/> Sat
23	<input type="checkbox"/> Sun	<input checked="" type="checkbox"/> Mon	<input checked="" type="checkbox"/> Tue	<input checked="" type="checkbox"/> Wed	<input checked="" type="checkbox"/> Thu	<input checked="" type="checkbox"/> Fri	<input type="checkbox"/> Sat

FIGURE 2B

Activity Table More Fields			
Category Fields			
Label1:	Account	Value1:	WalMart KMart CVS Eckerd
Label2:	Style	Value2:	Floorstand Sidekick
Label3:		Value3:	
Label4:		Value4:	
Label5:		Value5:	
Label6:		Value6:	
Label7:		Value7:	
Label8:		Value8:	
Label9:		Value9:	
Label10:		Value10:	
Customer Fields			
Label1:	Purchase Order Number		
Label2:	PO Quantity		
Label3:	Brand		
Label4:			
Label5:			
Label6:			
Label7:			
Label8:			
Label9:			
Label10:			
Label11:			
Label12:			
Label13:			
Label14:			
Label15:			

FIGURE 2C

Cross Reference Setup Parameters	
Continue	Cancel
Choose a Vendor and Customer for this relationship:	
Vendor:	<input type="text"/>
Customer/Div:	<input type="text"/>
Template Name:	<input type="text"/>

FIGURE 3

Activity Table More Fields			
Responsible			
#	Company	Customer Activity	Vendor Activity
	<input type="text" value="Customer"/>	<input type="text"/>	<input type="text"/>
		Add	Delete
1	Customer	Cost & Feasibility Form Initiated	Cost & Feasibility Form Initiated
2	Customer	Brand Approvals	Brand Approvals
3	Customer	Submit Design Development Request to Ve	Submit Design Development Request to Ve
4	Vendor	Structure Submitted to Customer	Structure Submitted to Customer
5	Customer	Structure Approved	Structure Approved
6	Vendor	Die-Lines Submitted to Art Agency	Die-Lines Submitted to Art Agency
7	Customer	Art Submitted to Customer by Agency	Art Submitted to Customer by Agency
8	Customer	Art Approved	Art Approved
9	Vendor	Specs Submitted for Pricing	Specs Submitted for Pricing
10	Vendor	Pricing Submitted to Customer	Pricing Submitted to Customer
11	Customer	Pricing Approved	Pricing Approved
12	Customer	Purchase Order Issued	Purchase Order Issued
13	Customer	Product Ordered	Product Ordered
14	Vendor	Work Order Submitted to Manufacturing	Work Order Submitted to Manufacturing
15	Vendor	Cutting Dies Ordered	Cutting Dies Ordered
16	Vendor	Printing Plates Ordered	Printing Plates Ordered
17	Vendor	Outside Parts Purchased	Outside Parts Purchased
18	Customer	All Proofs Approved	All Proofs Approved
19	Vendor	Component Manufacturing Start	Component Manufacturing Start
20	Vendor	Component Manufacturing Finish	Component Manufacturing Finish

FIGURE 4

09966710-092801
03260-0129650

Relationship Template : New Product Promotion		
Submit		Cancel
<input checked="" type="checkbox"/>	Enabled	
	Customer Information	Vendor Information
Name:	Home Products, Inc.	ABC Packaging Company
Division:	Consumer Division	Display Division
Project Contact:	James Grissom ▾	Nick Cornaglia ▾
Notification Users:	<div><input checked="" type="checkbox"/> James Grissom</div> <div><input type="checkbox"/> Kathy Cline</div> <div><input type="checkbox"/> Larry Shutzberg</div>	<div><input type="checkbox"/> Becca Spann</div> <div><input type="checkbox"/> Jack Ratcliff</div> <div><input checked="" type="checkbox"/> Nick Cornaglia</div>
Maintenance Users:	<div><input type="checkbox"/> James Grissom ▲</div> <div><input checked="" type="checkbox"/> Kathy Cline ▾</div> <div><input checked="" type="checkbox"/> Larry Shutzberg ▾</div> <div><input type="checkbox"/> BUYERS ▾</div>	<div><input type="checkbox"/> Becca Spann ▲</div> <div><input checked="" type="checkbox"/> Jack Ratcliff ▾</div> <div><input type="checkbox"/> Nick Cornaglia ▾</div> <div><input checked="" type="checkbox"/> DESIGNERS ▾</div>
Pending Attachments:	<div></div> <div></div>	<div>Add Attachment</div>

FIGURE 5

10666710-092801

Project Info More Info	
Customer Info	
Account:	<input type="text"/>
Style:	<input type="text"/>
Purchase Order Number:	<input type="text"/>
PO Quantity:	<input type="text"/>
Brand:	<input type="text"/>
Vendor Info	
Design Number:	<input type="text"/>
Manufactured Quantity:	<input type="text"/>
Assembled Quantity:	<input type="text"/>
QA Released Quantity:	<input type="text"/>
Shipped Quantity:	<input type="text"/>

FIGURE 5A

Activity Table More Fields					
Activities Workdays		Responsible Company	Responsible User	Seq	+Days
Seq.	Activity Name				
1	Cost & Feasibility Form Initiated	Customer	James Grissom		
2	Brand Approvals	Customer	James Grissom	1	2
3	Submit Design Development Request to Vendors	Customer	Kathy Cline	2	1
4	Structure Submitted to Customer	Vendor	Jack Ratcliff	3	5
5	Structure Approved	Customer	Kathy Cline	4	2
6	Die-Lines Submitted to Art Agency	Vendor	Jack Ratcliff	5	2
7	Art Submitted to Customer by Agency	Customer	Larry Shutzberg	6	5
8	Art Approved	Customer	Larry Shutzberg	7	2
9	Specs Submitted for Pricing	Vendor	Jack Ratcliff	8	2
10	Pricing Submitted to Customer	Vendor	Nick Cornaglia	9	2
11	Pricing Approved	Customer	James Grissom	10	1
12	Purchase Order Issued	Customer	Kathy Cline	11	2
13	Product Ordered	Customer	Kathy Cline	12	1
14	Work Order Submitted to Manufacturing	Vendor	Jack Ratcliff	12	1
15	Cutting Dies Ordered	Vendor	Nick Cornaglia	14	2
16	Printing Plates Ordered	Vendor	Nick Cornaglia	14	2
17	Outside Parts Purchased	Vendor	Jack Ratcliff	14	2

FIGURE 5B

Activities Workdays										Other Information
Seq.	Work Days									Other Info
1	<input type="checkbox"/> Sun	<input checked="" type="checkbox"/> Mon	<input checked="" type="checkbox"/> Tue	<input checked="" type="checkbox"/> Wed	<input checked="" type="checkbox"/> Thu	<input checked="" type="checkbox"/> Fri	<input type="checkbox"/> Sat			Other Info
2	<input type="checkbox"/> Sun	<input checked="" type="checkbox"/> Mon	<input checked="" type="checkbox"/> Tue	<input checked="" type="checkbox"/> Wed	<input checked="" type="checkbox"/> Thu	<input checked="" type="checkbox"/> Fri	<input type="checkbox"/> Sat			Other Info
3	<input type="checkbox"/> Sun	<input checked="" type="checkbox"/> Mon	<input checked="" type="checkbox"/> Tue	<input checked="" type="checkbox"/> Wed	<input checked="" type="checkbox"/> Thu	<input checked="" type="checkbox"/> Fri	<input type="checkbox"/> Sat			Other Info
4	<input type="checkbox"/> Sun	<input checked="" type="checkbox"/> Mon	<input checked="" type="checkbox"/> Tue	<input checked="" type="checkbox"/> Wed	<input checked="" type="checkbox"/> Thu	<input checked="" type="checkbox"/> Fri	<input type="checkbox"/> Sat			Other Info
5	<input type="checkbox"/> Sun	<input checked="" type="checkbox"/> Mon	<input checked="" type="checkbox"/> Tue	<input checked="" type="checkbox"/> Wed	<input checked="" type="checkbox"/> Thu	<input checked="" type="checkbox"/> Fri	<input type="checkbox"/> Sat			Other Info
6	<input type="checkbox"/> Sun	<input checked="" type="checkbox"/> Mon	<input checked="" type="checkbox"/> Tue	<input checked="" type="checkbox"/> Wed	<input checked="" type="checkbox"/> Thu	<input checked="" type="checkbox"/> Fri	<input type="checkbox"/> Sat			Other Info
7	<input type="checkbox"/> Sun	<input checked="" type="checkbox"/> Mon	<input checked="" type="checkbox"/> Tue	<input checked="" type="checkbox"/> Wed	<input checked="" type="checkbox"/> Thu	<input checked="" type="checkbox"/> Fri	<input type="checkbox"/> Sat			Other Info
8	<input type="checkbox"/> Sun	<input checked="" type="checkbox"/> Mon	<input checked="" type="checkbox"/> Tue	<input checked="" type="checkbox"/> Wed	<input checked="" type="checkbox"/> Thu	<input checked="" type="checkbox"/> Fri	<input type="checkbox"/> Sat			Other Info
9	<input type="checkbox"/> Sun	<input checked="" type="checkbox"/> Mon	<input checked="" type="checkbox"/> Tue	<input checked="" type="checkbox"/> Wed	<input checked="" type="checkbox"/> Thu	<input checked="" type="checkbox"/> Fri	<input type="checkbox"/> Sat			Other Info
10	<input type="checkbox"/> Sun	<input checked="" type="checkbox"/> Mon	<input checked="" type="checkbox"/> Tue	<input checked="" type="checkbox"/> Wed	<input checked="" type="checkbox"/> Thu	<input checked="" type="checkbox"/> Fri	<input type="checkbox"/> Sat			Other Info
11	<input type="checkbox"/> Sun	<input checked="" type="checkbox"/> Mon	<input checked="" type="checkbox"/> Tue	<input checked="" type="checkbox"/> Wed	<input checked="" type="checkbox"/> Thu	<input checked="" type="checkbox"/> Fri	<input type="checkbox"/> Sat			Other Info
12	<input type="checkbox"/> Sun	<input checked="" type="checkbox"/> Mon	<input checked="" type="checkbox"/> Tue	<input checked="" type="checkbox"/> Wed	<input checked="" type="checkbox"/> Thu	<input checked="" type="checkbox"/> Fri	<input type="checkbox"/> Sat			Other Info
13	<input type="checkbox"/> Sun	<input checked="" type="checkbox"/> Mon	<input checked="" type="checkbox"/> Tue	<input checked="" type="checkbox"/> Wed	<input checked="" type="checkbox"/> Thu	<input checked="" type="checkbox"/> Fri	<input type="checkbox"/> Sat			Other Info
14	<input type="checkbox"/> Sun	<input checked="" type="checkbox"/> Mon	<input checked="" type="checkbox"/> Tue	<input checked="" type="checkbox"/> Wed	<input checked="" type="checkbox"/> Thu	<input checked="" type="checkbox"/> Fri	<input type="checkbox"/> Sat			Other Info
15	<input type="checkbox"/> Sun	<input checked="" type="checkbox"/> Mon	<input checked="" type="checkbox"/> Tue	<input checked="" type="checkbox"/> Wed	<input checked="" type="checkbox"/> Thu	<input checked="" type="checkbox"/> Fri	<input type="checkbox"/> Sat			Other Info
16	<input type="checkbox"/> Sun	<input checked="" type="checkbox"/> Mon	<input checked="" type="checkbox"/> Tue	<input checked="" type="checkbox"/> Wed	<input checked="" type="checkbox"/> Thu	<input checked="" type="checkbox"/> Fri	<input type="checkbox"/> Sat			Other Info
17	<input type="checkbox"/> Sun	<input checked="" type="checkbox"/> Mon	<input checked="" type="checkbox"/> Tue	<input checked="" type="checkbox"/> Wed	<input checked="" type="checkbox"/> Thu	<input checked="" type="checkbox"/> Fri	<input type="checkbox"/> Sat			Other Info

FIGURE 5C

09965710-09201
T03250-0T799560

Name:	Customer Information	Vendor Information
Adv. Notification:	Home Products, Inc.	ABC Packaging Company
Notification Users:	<div>Days</div> <div><input checked="" type="checkbox"/> James Grissom <input type="checkbox"/> Kathy Cline <input type="checkbox"/> Larry Shutzberg</div>	<div>Days</div> <div><input type="checkbox"/> Becca Spann <input checked="" type="checkbox"/> Jack Ratcliff <input type="checkbox"/> Nick Cornaglia</div>
Maintenance Users:	<div><input type="checkbox"/> James Grissom <input checked="" type="checkbox"/> Kathy Cline <input type="checkbox"/> Larry Shutzberg <input type="checkbox"/> BUYERS</div>	<div><input type="checkbox"/> Becca Spann <input type="checkbox"/> Jack Ratcliff <input checked="" type="checkbox"/> Nick Cornaglia <input type="checkbox"/> DESIGNERS</div>
<div>OK Cancel</div>		

FIGURE 5D

Project Creation - Select Partner & Template
Continue Cancel

Customer:	<input type="radio"/> Home Products
Template:	<input type="radio"/> New Product Promotion

FIGURE 6

Project Creation - Project Info
Continue Cancel

BlueCuda #:	Will be automatically generated	
Project Name:	<input type="text"/> <input checked="" type="checkbox"/> Notify NOW!	
Name:	Customer Information	Vendor Information
Division:	Home Products, Inc.	ABC Packaging Company
Project Contact:	Consumer Division	Display Division
Item Number:	<input type="radio"/> James Grissom	<input type="radio"/> Nick Cornaglia
Project Status:		Open

FIGURE 7

Project Info More Info									
Product Information:									
Notes / Agreements:									
Pending Attachments:	<div>Add Attachment</div>								
Notification Users:	<table border="1"> <thead> <tr> <th>Customer Information</th> <th>Vendor Information</th> </tr> </thead> <tbody> <tr> <td><input checked="" type="checkbox"/> James Grissom</td> <td><input type="checkbox"/> Becca Spann</td> </tr> <tr> <td><input type="checkbox"/> Kathy Cline</td> <td><input type="checkbox"/> Jack Ratcliff</td> </tr> <tr> <td><input type="checkbox"/> Larry Shutzberg</td> <td><input checked="" type="checkbox"/> Nick Cornaglia</td> </tr> </tbody> </table>	Customer Information	Vendor Information	<input checked="" type="checkbox"/> James Grissom	<input type="checkbox"/> Becca Spann	<input type="checkbox"/> Kathy Cline	<input type="checkbox"/> Jack Ratcliff	<input type="checkbox"/> Larry Shutzberg	<input checked="" type="checkbox"/> Nick Cornaglia
Customer Information	Vendor Information								
<input checked="" type="checkbox"/> James Grissom	<input type="checkbox"/> Becca Spann								
<input type="checkbox"/> Kathy Cline	<input type="checkbox"/> Jack Ratcliff								
<input type="checkbox"/> Larry Shutzberg	<input checked="" type="checkbox"/> Nick Cornaglia								
Maintenance Users:	<table border="1"> <tbody> <tr> <td><input type="checkbox"/> James Grissom</td> <td><input type="checkbox"/> Becca Spann</td> </tr> <tr> <td><input checked="" type="checkbox"/> Kathy Cline</td> <td><input checked="" type="checkbox"/> Jack Ratcliff</td> </tr> <tr> <td><input checked="" type="checkbox"/> Larry Shutzberg</td> <td><input type="checkbox"/> Nick Cornaglia</td> </tr> <tr> <td><input type="checkbox"/> BUYERS</td> <td><input checked="" type="checkbox"/> DESIGNERS</td> </tr> </tbody> </table>	<input type="checkbox"/> James Grissom	<input type="checkbox"/> Becca Spann	<input checked="" type="checkbox"/> Kathy Cline	<input checked="" type="checkbox"/> Jack Ratcliff	<input checked="" type="checkbox"/> Larry Shutzberg	<input type="checkbox"/> Nick Cornaglia	<input type="checkbox"/> BUYERS	<input checked="" type="checkbox"/> DESIGNERS
<input type="checkbox"/> James Grissom	<input type="checkbox"/> Becca Spann								
<input checked="" type="checkbox"/> Kathy Cline	<input checked="" type="checkbox"/> Jack Ratcliff								
<input checked="" type="checkbox"/> Larry Shutzberg	<input type="checkbox"/> Nick Cornaglia								
<input type="checkbox"/> BUYERS	<input checked="" type="checkbox"/> DESIGNERS								

FIGURE 7A

FIGURE 8

Activity Information		Dates	Workdays	Completion Date		+Days	
Seq	Activity Name	Responsible User	Status	Planned	Actual	Seq	Orig New Plan
1	Cost & Feasibility Form Initiated	James Grissom	Cpl	08/16/2001	08/16/2001		
2	Brand Approvals	James Grissom	Hld	08/20/2001		1	2
3	Submit Design Development Request to Vendors	Kathy Cline	Opn	08/21/2001		2	1
4	Structure Submitted to Customer	Jack Ratcliff	Opn	08/28/2001		3	5
5	Structure Approved	Kathy Cline	Opn	08/30/2001		4	2
6	Die-Lines Submitted to Art Agency		Can				
7	Art Submitted to Customer by Agency		Can				
8	Art Approved	Larry Shutzberg	Opn	09/03/2001		5	2
9	Specs Submitted for Pricing	Jack Ratcliff	Opn	09/05/2001		8	2
10	Pricing Submitted to Customer	Nick Cornaglia	Opn	09/07/2001		9	2
11	Pricing Approved	James Grissom	Opn	09/10/2001		10	1
12	Purchase Order Issued	Kathy Cline	Opn	09/12/2001		11	2
13	Product Ordered	Kathy Cline	Opn	09/13/2001		12	1
14	Work Order Submitted to Manufacturing	Jack Ratcliff	Opn	09/13/2001		12	1
15	Cutting Dies Ordered	Nick Cornaglia	Opn	09/17/2001		14	2
16	Printing Plates Ordered	Nick Cornaglia	Opn	09/17/2001		14	2
17	Outside Parts Purchased	Jack Ratcliff	Opn	09/17/2001		14	2
18	All Proofs Approved	James Grissom	Opn	09/26/2001		16	7

FIGURE 9



FIGURE 10

	Customer	Vendor
Accept Close Delete	To:	
	<input type="checkbox"/> James Grissom <input type="checkbox"/> Kathy Cline <input type="checkbox"/> Larry Shutzberg	<input type="checkbox"/> Becca Spann <input type="checkbox"/> Jack Ratcliff <input type="checkbox"/> Nick Cornaglia
	cc:	
	<input type="checkbox"/> James Grissom <input type="checkbox"/> Kathy Cline <input type="checkbox"/> Larry Shutzberg	<input type="checkbox"/> Becca Spann <input type="checkbox"/> Jack Ratcliff <input type="checkbox"/> Nick Cornaglia
	bcc:	
	<input type="checkbox"/> James Grissom <input type="checkbox"/> Kathy Cline <input type="checkbox"/> Larry Shutzberg	<input type="checkbox"/> Becca Spann <input type="checkbox"/> Jack Ratcliff <input type="checkbox"/> Nick Cornaglia
Subject: Project Mgmt. Change Link		
Note: Email will be sent when the Project is submitted.		
<div></div>		

FIGURE 11

Add Activity (1 of 2)
Continue Cancel

BlueCuda #: 43
Project Name: Lemon Cough Drop Display

Activity Name: ●

Activity Owner: ●

Activity Type: ●

Insert Position ●

Before Activity:

After Activity:

FIGURE 12

Add Activity (2 of 2)
Accept Cancel

BlueCuda #: 43
Project Name: Lemon Cough Drop Display

Activity Name: Pricing Quote Approved
Activity Owner: Vendor
Activity Type: Shared

Responsible User: ●

Work Days: ● ☐ Sun ☒ Mon ☒ Tue ☒ Wed ☒ Thu ☒ Fri ☐ Sat

Notes/Agreements:

	Customer Information	Vendor Information
Name:	Home Products, Inc.	ABC Packaging Company
Adv. Notification:	<input type="text" value="Days"/>	<input type="text" value="Days"/>
Notification Users:	<input checked="" type="checkbox"/> James Grissom <input type="checkbox"/> Kathy Cline <input type="checkbox"/> Larry Shutzberg	<input type="checkbox"/> Becca Spann <input type="checkbox"/> Jack Ratcliff <input checked="" type="checkbox"/> Nick Cornaglia
Maintenance Users:	<input type="checkbox"/> James Grissom <input type="checkbox"/> Kathy Cline <input type="checkbox"/> Larry Shutzberg <input type="checkbox"/> BUYERS	<input type="checkbox"/> Becca Spann <input type="checkbox"/> Jack Ratcliff <input type="checkbox"/> Nick Cornaglia <input type="checkbox"/> DESIGNERS

FIGURE 12A

Structure Submitted to Customer			
Submit		Cancel	
BlueCuda #:	49		
Project Name:	Back to School Promo		<input type="checkbox"/> Notify NOW!
		Customer Information	Vendor Information
Name:	Home Products, Inc.		ABC Packaging Company
Division:	Consumer Division		Display Division
Project Contact:	Larry Shutzberg		Nick Cornaglia
Responsible User:	<div> <div>Jack Ratcliff</div> <div></div> </div>		
Third Party:	<div> <div></div> <div></div> </div>		
Activity Status:	Open		
Workdays:	Mon, Tue, Wed, Thu, Fri		
	Planned	Actual	
Completion Date:	07/11/2001	<div> <div></div> <div></div> </div>	<div> <div>Today</div> <div>Yesterday</div> </div>
Notes/Agreements:	<div> <div></div> <div></div> </div>		
Pending Attachments:	<div> <div></div> <div></div> </div> <div>Add Attachment</div>		

FIGURE 13



FIGURE 14

My Projects		Grouping: Ungrouped		Show: Late	
New Project	Expand	Collapse	Previous	Next	Top
Update Selected Activities		GoTo			
Activity		Responsibility	Planned	Actual	
... Cherry Fizzy Antacid SK - 45 (Home Products)					
● Structure Approved	Kathy Cline	Opn	8/28/01		Y T
... Lemon Cough Drop Display - 43 (Home Products)					
● Brand Approvals	James Grissom	Hld	8/20/01		Y T
● Submit Design Development Request to Vendors	Kathy Cline	Opn	8/21/01		Y T
● Structure Submitted to Customer	Jack Ratcliff	Opn	8/28/01		Y T

FIGURE 14A

My Projects by Plan Date		Grouping: Ungrouped		Show: All	
New Project	Expand	Collapse	Previous	Next	Top
Update Selected Activities		GoTo			
Project	Activity	Partner	Responsibility	Planned	Actual
08/2001					
Cherry Fizzy Antacid SK - 45	● Cost & Feasibility Form Initiated	Home Products	James Grissom Cpl	8/15/01	08/16/2001 Y T
Lemon Cough Drop Display - 43	● Cost & Feasibility Form Initiated	Home Products	James Grissom Cpl	8/16/01	08/16/2001 Y T
Cherry Fizzy Antacid SK - 45	● Brand Approvals	Home Products	James Grissom Cpl	8/17/01	08/16/2001 Y T
Lemon Cough Drop Display - 43	● Brand Approvals	Home Products	James Grissom Hld	8/20/01	Y T

FIGURE 14B

096670-096670

My Projects by Activity				Grouping: Ungrouped		Show: Open	
New Project		Expand	Collapse	Previous	Next	Top	GoTo
Update Selected Activities							
Project	Activity	Partner	Responsibility	Planned	Actual		
All Proofs Approved							
Lemon Cough Drop Display - 43	All Proofs Approved	Home Products	James Grissom	Opn 9/26/01			Y T
Art Approved							
Lemon Cough Drop Display - 43	Art Approved	Home Products	Larry Shutzberg	Opn 9/03/01			Y T
Cherry Fizzy Antacid SK - 45	Art Approved	Home Products	Larry Shutzberg	Opn 9/10/01			Y T
Art Submitted to Customer by Agency							
Cherry Fizzy Antacid SK - 45	Art Submitted to Customer by Agency	Home Products	Larry Shutzberg	Opn 9/06/01			Y T
Assembly Finish							
Lemon Cough Drop Display - 43	Assembly Finish	Home Products	Jack Ratcliff	Opn 10/15/01			Y T
Cherry Fizzy Antacid SK - 45	Assembly Finish	Home Products	Jack Ratcliff	Opn 10/22/01			Y T
Assembly Start							
Lemon Cough Drop Display - 43	Assembly Start	Home Products	Nick Cornaglia	Opn 10/08/01			Y T
Cherry Fizzy Antacid SK - 45	Assembly Start	Home Products	Nick Cornaglia	Opn 10/15/01			Y T
Component Manufacturing Finish							
Lemon Cough Drop Display - 43	Component Manufacturing Finish	Home Products	Jack Ratcliff	Opn 10/04/01			Y T

FIGURE 14C

- My Activities
 - Project
 - Plan Date
 - Activity

FIGURE 15

My Activities by Project				Grouping: Ungrouped	Show: Late
New Project		Expand	Collapse	Previous	Next
Update Selected Activities		Top GoTo			
Activity	Responsibility		Planned	Actual	
<div> <div>...</div> <div>20523823FS Summer Cold Caps 50 - 48 (Home Products)</div> </div> <div> <div>Structure Submitted to Customer</div> <div>Jack Ratcliff</div> </div>	Opn	8/24/01		Y T	
<div> <div>--</div> <div>2546925SK Spring Allergy Tabs - 47 (Home Products)</div> </div> <div> <div>Structure Submitted to Customer</div> <div>Jack Ratcliff</div> </div>	Opn	8/15/01		Y T	
<div> <div>Die-Lines Submitted to Art Agency</div> <div>Jack Ratcliff</div> </div>	Opn	8/21/01		Y T	
<div> <div>...</div> <div>a test - 081701 - 52 (Home Products)</div> </div> <div> <div>Structure Submitted to Customer</div> <div>Jack Ratcliff</div> </div>	Opn	8/29/01		Y T	

FIGURE 15A

My Activities by Plan Date				Grouping: Ungrouped	Show: Open
New Project		Expand	Collapse	Previous	Next
Update Selected Activities		Top GoTo			
Project	Activity	Partner	Responsibility	Planned	Actual
07/2001					
Back to School Promo - 49	Structure Submitted to Customer	Home Products	Jack Ratcliff	Opn 7/11/01	Y T
Back to School Promo - 49	Die-Lines Submitted to Art Agency	Home Products	Jack Ratcliff	Opn 7/17/01	Y T
Back to School Promo - 49	Specs Submitted for Pricing	Home Products	Jack Ratcliff	Opn 7/30/01	Y T
08/2001					
Winter Flu Tablets 64 - 44	Specs Submitted for Pricing	Home Products	Jack Ratcliff	Opn 8/06/01	Y T
Back to School Promo - 49	Work Order Submitted to Manufacturing	Home Products	Jack Ratcliff	Opn 8/07/01	Y T

FIGURE 15B

My Activities by Activity			Grouping: Ungrouped		Show: Late		
New Project		Expand	Collapse	Previous	Next	Top	GoTo
Update Selected Activities							
Project		Activity	Partner	Responsibility	Planned	Actual	
Component Manufacturing Finish							
Back to School Promo - 49		Component Manufacturing Finish	Home Products	Jack Ratcliff	Opn 8/28/01		
Die-Lines Submitted to Art Agency							
Back to School Promo - 49		Die-Lines Submitted to Art Agency	Home Products	Jack Ratcliff	Opn 7/17/01		
2546925SK Spring Allergy Tabs - 47		Die-Lines Submitted to Art Agency	Home Products	Jack Ratcliff	Opn 8/21/01		
Outside Parts Purchased							
Back to School Promo - 49		Outside Parts Purchased	Home Products	Jack Ratcliff	Opn 8/09/01		
Winter Flu Tablets 64 - 44		Outside Parts Purchased	Home Products	Jack Ratcliff	Opn 8/16/01		
Holiday Lipgloss Display - 53		Outside Parts Purchased	Home Products	Jack Ratcliff	Opn 8/23/01		

FIGURE 15C

- Company Views
 - Project
 - Plan Date
 - Activity
 - Responsibility
 - Activity
 - Plan Date
 - Responsibility
 - Responsibility
 - Plan Date
 - Activity
 - 3rd Party

FIGURE 16

0966710-092601

Projects		Grouping: Ungrouped		Show: Late		
New Project	Expand	Collapse	Previous	Next	Top	GoTo
Activity		Responsibility		Planned		Actual
...	2546925SK Spring Allergy Tabs - 47 (Home Products)					
	Structure Submitted to Customer	Jack Ratcliff	Opn	8/15/01	---	
...	Back to School Promo - 49 (Home Products)					
	Cost & Feasibility Form Initiated	James Grissom	Opn	7/01/01	---	
	Brand Approvals	James Grissom	Opn	7/03/01	---	
	Submit Design Development Request to Vendors	Kathy Cline	Opn	7/04/01	---	
	Structure Submitted to Customer	Jack Ratcliff	Opn	7/11/01	---	
	Structure Approved	Kathy Cline	Opn	7/13/01	---	
	Die-Lines Submitted to Art Agency	Jack Ratcliff	Opn	7/17/01	---	
	Art Submitted to Customer by Agency	Larry Shutzberg	Opn	7/24/01	---	
	Art Approved	Larry Shutzberg	Opn	7/26/01	---	
	Specs Submitted for Pricing	Jack Ratcliff	Opn	7/30/01	---	
	Pricing Submitted to Customer	Nick Cornaglia	Opn	8/01/01	---	
	Pricing Approved	James Grissom	Opn	8/02/01	---	
	Purchase Order Issued	Kathy Cline	Opn	8/06/01	---	
	Product Ordered	Kathy Cline	Opn	8/07/01	---	
	Work Order Submitted to Manufacturing	Jack Ratcliff	Opn	8/07/01	---	
	Cutting Dies Ordered	Nick Cornaglia	Opn	8/09/01	---	
	Printing Plates Ordered	Nick Cornaglia	Opn	8/09/01	---	
	Outside Parts Purchased	Jack Ratcliff	Opn	8/09/01	---	
...	Headache Gel Caps 24 - 50 (Home Products)					
	Cost & Feasibility Form Initiated	James Grissom	Opn	8/16/01	---	
	Brand Approvals	James Grissom	Opn	8/20/01	---	
	Submit Design Development Request to Vendors	Kathy Cline	Opn	8/21/01	---	
...	Headache Gel Caps 24 - 51 (Home Products)					
	Cost & Feasibility Form Initiated	James Grissom	Opn	8/16/01	---	

FIGURE 16A

















Activities by Date/Activity			Grouping: <div>Ungrouped</div>		Show: <div>Open</div>	
New Project	Expand	Collapse	Previous	Next	Top	GoTo
Project	Activity	Partner	Responsibility	Planned	Actual	
<div>07/2001</div>						
<div>Art Approved</div>						
Back to School Promo - 49 	 Art Approved	Home Products	Larry Shutzberg	Opn	7/26/01	---
<div>Art Submitted to Customer by Agency</div>						
Back to School Promo - 49 	 Art Submitted to Customer by Agency	Home Products	Larry Shutzberg	Opn	7/24/01	---
<div>Brand Approvals</div>						
Back to School Promo - 49 	 Brand Approvals	Home Products	James Grissom	Opn	7/03/01	---
<div>Cost & Feasibility Form Initiated</div>						
Back to School Promo - 49 	 Cost & Feasibility Form Initiated	Home Products	James Grissom	Opn	7/01/01	---
<div>Die-Lines Submitted to Art Agency</div>						
Back to School Promo - 49 	 Die-Lines Submitted to Art Agency	Home Products	Jack Ratcliff	Opn	7/17/01	---
<div>Specs Submitted for Pricing</div>						
Back to School Promo - 49 	 Specs Submitted for Pricing	Home Products	Jack Ratcliff	Opn	7/30/01	---
<div>Structure Approved</div>						
Back to School Promo - 49 	 Structure Approved	Home Products	Kathy Cline	Opn	7/13/01	---
Winter Flu Tablets 64 - 44 	 Structure Approved	Home Products	Kathy Cline	Opn	7/20/01	---

FIGURE 16B

Activities by Date/User			Grouping: Ungrouped		Show: Open	
New Project	Expand	Collapse	Previous	Next	Top	GoTo
Project		Activity	Partner	Responsibility	Planned	Actual
07/2001						
Jack Ratcliff						
Back to School Promo - 49		Structure Submitted to Customer	Home Products	Jack Ratcliff	Opn	7/11/01 ---
Back to School Promo - 49		Die-Lines Submitted to Art Agency	Home Products	Jack Ratcliff	Opn	7/17/01 ---
Back to School Promo - 49		Specs Submitted for Pricing	Home Products	Jack Ratcliff	Opn	7/30/01 ---
James Grissom						
Back to School Promo - 49		Cost & Feasibility Form Initiated	Home Products	James Grissom	Opn	7/01/01 ---
Back to School Promo - 49		Brand Approvals	Home Products	James Grissom	Opn	7/03/01 ---
Kathy Cline						
Back to School Promo - 49		Submit Design Development Request to Vendors	Home Products	Kathy Cline	Opn	7/04/01 ---
Back to School Promo - 49		Structure Approved	Home Products	Kathy Cline	Opn	7/13/01 ---
Winter Flu Tablets 64 - 44		Structure Approved	Home Products	Kathy Cline	Opn	7/20/01 ---
Larry Shutzberg						
Back to School Promo - 49		Art Submitted to Customer by Agency	Home Products	Larry Shutzberg	Opn	7/24/01 ---
Back to School Promo - 49		Art Approved	Home Products	Larry Shutzberg	Opn	7/26/01 ---

FIGURE 16C

095670-095674

Activities by Activity/Date		Grouping: Ungrouped		Show: Open	
New Project	Expand	Collapse	Previous	Next	Top
GoTo					
Project	Activity	Partner	Responsibility	Planned	Actual
All Proofs Approved					
08/2001					
Back to School Promo - 49	All Proofs Approved	Home Products	James Grissom	Opn	8/20/01
Winter Flu Tablets 64 - 44	All Proofs Approved	Home Products	James Grissom	Opn	8/27/01
09/2001					
Holiday Lipgloss Display - 53	All Proofs Approved	Home Products	James Grissom	Opn	9/03/01
Lemon Cough Drop Display - 43	All Proofs Approved	Home Products	James Grissom	Opn	9/26/01
10/2001					
20523823FS Summer Cold Caps 50 - 48	All Proofs Approved	Home Products	James Grissom	Opn	10/03/01
Headache Gel Caps 24 - 50	All Proofs Approved	Home Products	James Grissom	Opn	10/03/01
Wal-Mart Candy Display - 42	All Proofs Approved	Home Products	James Grissom	Opn	10/04/01
Summer Sunscreen Promo - 46	All Proofs Approved	Home Products	James Grissom	Opn	10/04/01
a test - 081701 - 52	All Proofs Approved	Home Products	James Grissom	Opn	10/08/01

Headache Gel Caps 24 - 51	All Proofs Approved	Home Products	James Grissom	Opn	---

FIGURE 16D

108250-0749550

Activities by Activity/User				Grouping: Ungrouped		Show: Late	
New Project		Expand	Collapse	Previous	Next	Top	GoTo
Project		Activity		Partner	Responsibility	Planned	Actual
Art Approved							
Larry Shutzberg							
Back to School Promo - 49		Art Approved	Home Products	Larry Shutzberg	Opn	7/26/01	---
Winter Flu Tablets 64 - 44		Art Approved	Home Products	Larry Shutzberg	Opn	8/02/01	---
Art Submitted to Customer by Agency							
Larry Shutzberg							
Back to School Promo - 49		Art Submitted to Customer by Agency	Home Products	Larry Shutzberg	Opn	7/24/01	---
Brand Approvals							
James Grissom							
Back to School Promo - 49		Brand Approvals	Home Products	James Grissom	Opn	7/03/01	---
20523823FS Summer Cold Caps 50 - 48		Brand Approvals	Home Products	James Grissom	Opn	8/16/01	---
Lemon Cough Drop Display - 43		Brand Approvals	Home Products	James Grissom	Hld	8/20/01	---
Headache Gel Caps 24 - 50		Brand Approvals	Home Products	James Grissom	Opn	8/20/01	---
Cost & Feasibility Form Initiated							
James Grissom							
Back to School Promo - 49		Cost & Feasibility Form Initiated	Home Products	James Grissom	Opn	7/01/01	---
Wal-Mart Candy Display - 42		Cost & Feasibility Form Initiated	Home Products	James Grissom	Opn	8/15/01	---

FIGURE 16E

Activities by User/Date		Grouping: Ungrouped		Show: Completed		
New Project	Expand	Collapse	Previous	Next	Top	GoTo
Project	Activity	Partner	Responsibility	Planned	Actual	
Jack Ratcliff						
07/2001						
Winter Flu Tablets 64 - 44	Structure Submitted to Customer	Home Products	Jack Ratcliff	Cpl	7/18/01	7/18/01
Winter Flu Tablets 64 - 44	Die-Lines Submitted to Art Agency	Home Products	Jack Ratcliff	Cpl	7/24/01	7/24/01
Holiday Lipgloss Display - 53	Structure Submitted to Customer	Home Products	Jack Ratcliff	Cpl	7/25/01	7/25/01
Holiday Lipgloss Display - 53	Die-Lines Submitted to Art Agency	Home Products	Jack Ratcliff	Cpl	7/31/01	7/31/01
08/2001						
Holiday Lipgloss Display - 53	Specs Submitted for Pricing	Home Products	Jack Ratcliff	Cpl	8/13/01	8/13/01
Holiday Lipgloss Display - 53	Work Order Submitted to Manufacturing	Home Products	Jack Ratcliff	Cpl	8/21/01	8/21/01
Cherry Fizzy Antacid SK - 45	Structure Submitted to Customer	Home Products	Jack Ratcliff	Cpl	8/24/01	8/16/01
James Grissom						
07/2001						
Winter Flu Tablets 64 - 44	Cost & Feasibility Form Initiated	Home Products	James Grissom	Cpl	7/06/01	8/10/01
Winter Flu Tablets 64 - 44	Brand Approvals	Home Products	James Grissom	Cpl	7/10/01	8/10/01
Holiday Lipgloss Display - 53	Cost & Feasibility Form Initiated	Home Products	James Grissom	Cpl	7/13/01	7/13/01
Holiday Lipgloss Display - 53	Brand Approvals	Home Products	James Grissom	Cpl	7/17/01	7/17/01

FIGURE 16F

0966740-0966740

Activities by User/Activity			Grouping: Ungrouped		Show: Completed	
New Project	Expand	Collapse	Previous	Next	Top	GoTo
Project		Activity	Partner	Responsibility	Planned	Actual
Jack Ratcliff						
Die-Lines Submitted to Art Agency						
Winter Flu Tablets 64 - 44		Die-Lines Submitted to Art Agency	Home Products	Jack Ratcliff	Cpl	7/24/01 7/24/01
Holiday Lipgloss Display - 53		Die-Lines Submitted to Art Agency	Home Products	Jack Ratcliff	Cpl	7/31/01 7/31/01
Specs Submitted for Pricing						
Holiday Lipgloss Display - 53		Specs Submitted for Pricing	Home Products	Jack Ratcliff	Cpl	8/13/01 8/13/01
Structure Submitted to Customer						
Winter Flu Tablets 64 - 44		Structure Submitted to Customer	Home Products	Jack Ratcliff	Cpl	7/18/01 7/18/01
Holiday Lipgloss Display - 53		Structure Submitted to Customer	Home Products	Jack Ratcliff	Cpl	7/25/01 7/25/01
Cherry Fizzy Antacid SK - 45		Structure Submitted to Customer	Home Products	Jack Ratcliff	Cpl	8/24/01 8/16/01
Work Order Submitted to Manufacturing						
Holiday Lipgloss Display - 53		Work Order Submitted to Manufacturing	Home Products	Jack Ratcliff	Cpl	8/21/01 8/21/01
James Grissom						
All Proofs Approved						
2546925SK Spring Allergy Tabs - 47		All Proofs Approved	Home Products	James Grissom	Cpl	9/24/01 8/17/01
Brand Approvals						
Winter Flu Tablets 64 - 44		Brand Approvals	Home Products	James Grissom	Cpl	7/10/01 8/10/01
Holiday Lipgloss Display - 53		Brand Approvals	Home Products	James Grissom	Cpl	7/17/01 7/17/01

FIGURE 16G









Activities by 3rd Party							
New Project	Expand	Collapse	Previous	Next	Top	GoTo	
Project		Activity	Partner	Responsibility		Planned	Actual
 ABC, Inc.							
Back to School Promo - 49		 Die-Lines Submitted to Art Agency	Home Products	Jack Ratcliff	Opn	7/17/01	---
Wal-Mart Candy Display - 42		 Work Order Submitted to Manufacturing	Home Products	Jack Ratcliff	Opn	9/21/01	---
 Arolston Inc.							
Winter Flu Tablets 64 - 44		 Component Manufacturing Finish	Home Products	Jack Ratcliff	Opn	9/04/01	---

FIGURE 16H

Grouping: **Ungrouped** ▼

apse Pre **--Select One--**

Respo **Ungrouped**

Customer

FIGURE 17

Show: **Open** ▼

Top **--Select One--**

Plan All

6/01 All w/o Can

5 (P&G) Held

9/04 Late

8/31 **Open**

Open/Held

Completed

Canceled

FIGURE 18

1. Build your search Search Now Clear Entries
Fill out **at least one** of the following fields

<p>Document Types</p> <p><input checked="" type="checkbox"/> Project <input type="checkbox"/> Activity</p> <p>Project Name</p> <p>_____</p> <p>Activity Name</p> <p>_____</p> <p>Planned Completion Date</p> <p>From: _____</p> <p>To: _____</p> <p>Company Name</p> <p>_____</p>	<p>Word(s)</p> <p>_____</p> <p>Project Contact</p> <p>_____</p> <p>Activity Responsible User</p> <p>_____</p> <p>Actual Completion Date</p> <p>From: _____</p> <p>To: _____</p> <p>Division</p> <p>_____</p>	<p>All words ▼</p> <p>Blue Cuda #</p> <p>_____</p>
--	---	--

2. Optional: Refine your search Search Now Clear Entries
Fill out **one or more** of the following fields

Max Nbr of docs: **All** ▼ Nbr per page: **10** ▼ Sort by: **Keep Original Sort Order** ▼

☐ **Use word variants & fuzzy search**

Use word variants

Also find variations on your words. For example, a search for create will also find creates, creating, created, and creator.

Use fuzzy search

Find similar words or phrases. Even finds misspelled words. For example, a search for pakaging will also find packaging.

FIGURE 19

BlueCuda Newsletter for lshutzberg

MY :	Late Activities	Advance Notification	New	Orphaned	Other Changes
Other :	Late Activities	Advance Notification	New	Orphaned	Other Changes

MY LATE ACTIVITIES

Project: [Winter Flu Tablets 64 \(44\)](#) **Vendor:** ABC Packaging Company

Activity: [Art Approved \(Open\)](#) **Resp:** Larry Shutzberg (Cust) **Due:** 08/02/2001

Project: [Back to School Promo \(49\)](#) **Vendor:** ABC Packaging Company

Activity: [Art Approved \(Open\)](#) **Resp:** Larry Shutzberg (Cust) **Due:** 07/26/2001

[Return to top](#)

MY ADVANCE NOTIFICATIONS

Project: [Lemon Cough Drop Display \(43\)](#) **Vendor:** ABC Packaging Company

Activity: [Art Approved \(Open\)](#) **Resp:** Larry Shutzberg (Cust) **Due:** 09/03/2001

Project: [2546925SK Spring Allergy Tabs \(47\)](#) **Vendor:** ABC Packaging Company

Activity: [Art Submitted to Customer by Agency \(Open\)](#) **Resp:** Larry Shutzberg (Cust) **Due:** 08/28/2001

Activity: [Art Approved \(Open\)](#) **Resp:** Larry Shutzberg (Cust) **Due:** 08/30/2001

[Return to top](#)

MY NEW PROJECTS AND ACTIVITIES

Project: [Winter Flu Tablets 64 \(44\)](#) **Vendor:** ABC Packaging Company

Activity: [Art Approved \(Open\)](#) **Resp:** Larry Shutzberg (Cust) **Due:** 08/02/2001

Project: [2546925SK Spring Allergy Tabs \(47\)](#) **Vendor:** ABC Packaging Company

Activity: [Art Submitted to Customer by Agency \(Open\)](#) **Resp:** Larry Shutzberg (Cust) **Due:** 08/28/2001

Activity: [Art Approved \(Open\)](#) **Resp:** Larry Shutzberg (Cust) **Due:** 08/30/2001

[Return to top](#)

MY ORPHANED ACTIVITIES

Nothing to Report

[Return to top](#)

MY CHANGED PROJECTS AND ACTIVITIES

Project: [Cherry Fizzy Antacid SK \(45\)](#) **Customer:** Home Products, Inc. / Consumer Division

Activity: [Art Approved \(Open\)](#) **Resp:** Larry Shutzberg (Cust) **Due:** 09/10/2001

Added Attachments :

Production Memo.doc on 8/16/01 10:45:19 AM - Larry Shutzberg

FIGURE 20

OTHER LATE ACTIVITIES

Project: Summer Sunscreen Promo (46) **Vendor:** ABC Packaging Company

Activity: Submit Design Development Request to Vendors (Open) **Resp:** Kathy Cline (Cust) **Due:** 08/20/2001

Project: Back to School Promo (49) **Vendor:** ABC Packaging Company

Activity: Submit Design Development Request to Vendors (Open) **Resp:** Kathy Cline (Cust) **Due:** 07/04/2001

[Return to top](#)

OTHER ADVANCE NOTIFICATIONS

Nothing to Report

[Return to top](#)

OTHER NEW PROJECTS AND ACTIVITIES

Nothing to Report

[Return to top](#)

OTHER ORPHANED ACTIVITIES

Nothing to Report

[Return to top](#)

OTHER CHANGED PROJECTS AND ACTIVITIES

Project: 2546925SK Spring Allergy Tabs (47) **Customer:** Home Products, Inc. / Consumer Division

Activity: Submit Design Development Request to Vendors (Completed) **Resp:** Kathy Cline (Cust)
Due: 08/08/2001

Activity Status Change :

Activity Status Open to Completed on 8/16/01 11:00:40 AM - Larry Shutzberg

Actual Completion Date Change :

Actual Completion date 8/8/01 8/16/01 11:00:40 AM - Larry Shutzberg

Added Attachments :

Production Memo.doc on 8/16/01 11:00:40 AM - Larry Shutzberg

Other Changes :

The activity was changed 8/16/01 11:00:40 AM - Larry Shutzberg

[Return to top](#)

FIGURE 20A

BlueCuda Web Reporting

This may take several minutes depending on the number of projects available.

Please select one of the following customers

then select one of the following reports

Click <OK> to continue or <Cancel> to return to previous view.

OK

Cancel

FIGURE 21

BlueCuda Report Selection -- Web Page Dialog

BlueCuda Reporting: Selection Criteria

Preview Cancel

Select items to include on report --

Project Types (<input type="checkbox"/> ignore)	Project Status (<input type="checkbox"/> ignore)
<input type="checkbox"/> All <input type="checkbox"/> Assumed <input type="button" value="Select All"/> <input type="button" value="Unselect All"/>	<input type="checkbox"/> [blank] <input type="checkbox"/> Custom <input type="checkbox"/> Forecasted <input type="checkbox"/> Promotional

Business Units (<input type="checkbox"/> ignore)	Brands (<input checked="" type="checkbox"/> ignore)
<input type="checkbox"/> All <input type="checkbox"/> Assumed <input type="button" value="Select All"/> <input type="button" value="Unselect All"/>	

Component Vendors (<input type="checkbox"/> ignore)	Assembly Vendors (<input type="checkbox"/> ignore)
<input type="checkbox"/> All <input type="checkbox"/> Assumed <input type="button" value="Select All"/> <input type="button" value="Unselect All"/>	<input type="checkbox"/> [blank] <input type="checkbox"/> Alliance <input type="checkbox"/> Altwell <input type="checkbox"/> Blauvelt

Accounts (<input type="checkbox"/> ignore)
<input type="checkbox"/> All <input type="checkbox"/> Assumed <input type="button" value="Select All"/> <input type="button" value="Unselect All"/>

Sort By --

- ☐ BlueCuda #
- ☐ Customer Item #
- ☐ Component Production Start Date
- ☐ Assembly Start Date
- ☐ Ship to AHP DCs Date
- ☐ Ship to Account DCs Date
- ☒ Arrive at Account DCs Date

(the dates above are planned dates)

Include --

- ☒ Product Info
- ☐ Notes / Agreements

FIGURE 21A

BlueCuda™			ABC Consumer Products Company										Production Scheduling										As of 8/1/01 @ 7:06 PM All dates shown as planned over actual									
Sorted by: Active in Account DCs Planned Date																																
BlueCuda Order #	Project Name	Style	Account	Component Vendor	Forecasted Quantity	PO Quantity	Component Mfg Quantity	Assembly Quantity	QA Released Quantity	Shipped Quantity	Schedule Production in AS	Schedule Assembly Packout	Product Order	Component Production Start	Component Production Finish	Component Arrive at Assembly	Product Arrives at Assembly	Assembly Start	Assembly Finish	Final QA Release	Ship to Alt DCs	Ship to Account DCs	Arrive at Account DCs	Status								
457	861704	861704	PDQ	KMA	TB	AM	3,700				8/28	8/14	8/21	8/20	8/24	8/10	8/17	8/20	8/21	8/24	10/01	10/10	Open									
861704	861704	861704	PDQ	KMA	AM	AM	3,000				8/27	8/13	8/20	8/20	8/31	8/07	8/14	8/21	8/24	10/01	10/08	10/15	Open									
454	862384	862384	PDQ	KMA	AM	AM	3,000				8/22																					
862384	862384	862384	PDQ	KMA	TB	AM	3,700				8/16	8/10	8/17	8/26	8/28	10/04	10/11	10/18	10/19	10/25	11/02	11/09	Open									
456	223087	223087	PDQ	KMA	AM	AM	3,000				8/24	8/10	8/20	10/05	10/08	10/15	10/22	10/29	10/30	11/05	11/12	11/20	Open									
862384	862384	862384	PDQ	KMA	AM	AM	3,000				8/24	8/10	8/20	10/05	10/08	10/15	10/22	10/29	10/30	11/05	11/12	11/20	Open									
453	863752	863752	FS/SK	WLC	AM	AM	4,000				9/04	8/27	10/04	10/14	10/17	10/23	10/30	11/06	11/13	11/21	11/28	Open										
863752	863752	863752	FS/SK	WLC	AM	AM	4,000				9/04	8/27	10/04	10/14	10/17	10/23	10/30	11/06	11/13	11/21	11/28	Open										
Projects selected 5 of 5																																

Projects selected: 5 of 5

FIGURE 21B

09566710 09566710

ACTIVITY STATUSES	BUSINESS RULES
Open	<ul style="list-style-type: none"> • Automatically defaulted to Open for newly created project activities. • Automatically set to Open when “Release” option is selected on a Held project activity or “Uncancel” option is selected on a Canceled project activity. • Automatically set to Open when ACTUAL COMPLETION DATE is removed from a project activity. • Automatically set to Open for all viewable Held project activities when “Release All” is selected. • Automatically set to Open for all viewable Canceled project activities when “Uncancel All” is selected. “Uncancel All” only affects Canceled project activities.
Held	<ul style="list-style-type: none"> • Automatically set to Held when “Hold” option is selected on an Open or Canceled project activity. Only an Open or Canceled project activity can become Held. • Automatically set to Held for all viewable Open project activities when “Hold All” is selected. “Hold All” only affects Open project activities.
Canceled	<ul style="list-style-type: none"> • Automatically set to Canceled when “Cancel” option is selected on an Open or Held project activity. Only an Open or Held project activity can become Canceled. • Automatically set to Canceled for all viewable Open project activities when “Cancel All” is selected. “Cancel All” only affects Open project activities.
Completed	<ul style="list-style-type: none"> • Automatically set to Completed when ACTUAL COMPLETION DATE is entered on a project activity.

FIGURE 22

PROJECT STATUSES	BUSINESS RULES
Open	<ul style="list-style-type: none"> Automatically set to Open if at least one viewable project activity is Open. Other viewable project activities can be Open, Held, Canceled, or Completed.
Held	<ul style="list-style-type: none"> Automatically set to Held if no viewable project activities are Open and at least one viewable project activity is Held. Other viewable project activities can be Held, Canceled, or Completed.
Canceled	<ul style="list-style-type: none"> Automatically set to Canceled if all viewable project activities are either Canceled or Completed and the last viewable project activity is Canceled.
Completed	<ul style="list-style-type: none"> Automatically set to Completed if all viewable project activities are either Canceled or Completed and the last viewable project activity is Completed.

FIGURE 23

USER TYPE	USER CHARACTERISTICS
Customer Lead User (w/ Administration)	User defined for a Customer with LEAD USER = Yes and ADMINISTRATION USER = Yes.
Customer Lead User (w/o Administration)	User defined for a Customer with LEAD USER = Yes and ADMINISTRATION USER = No.
Customer Non-Lead User	User defined for a Customer with LEAD USER = No (ADMINISTRATION USER will automatically be No).
Vendor Lead User (w/ Administration)	User defined for a Vendor with LEAD USER = Yes and ADMINISTRATION USER = Yes.
Vendor Lead User (w/o Administration)	User defined for a Vendor with LEAD USER = Yes and ADMINISTRATION USER = No.
Vendor Non-Lead User	User defined for a Vendor with LEAD USER = No (ADMINISTRATION USER will automatically be No).
3rd Party User	User defined for a 3rd Party.
Administrator	User defined as an Administrator.

FIGURE 24

103250 DT 9360

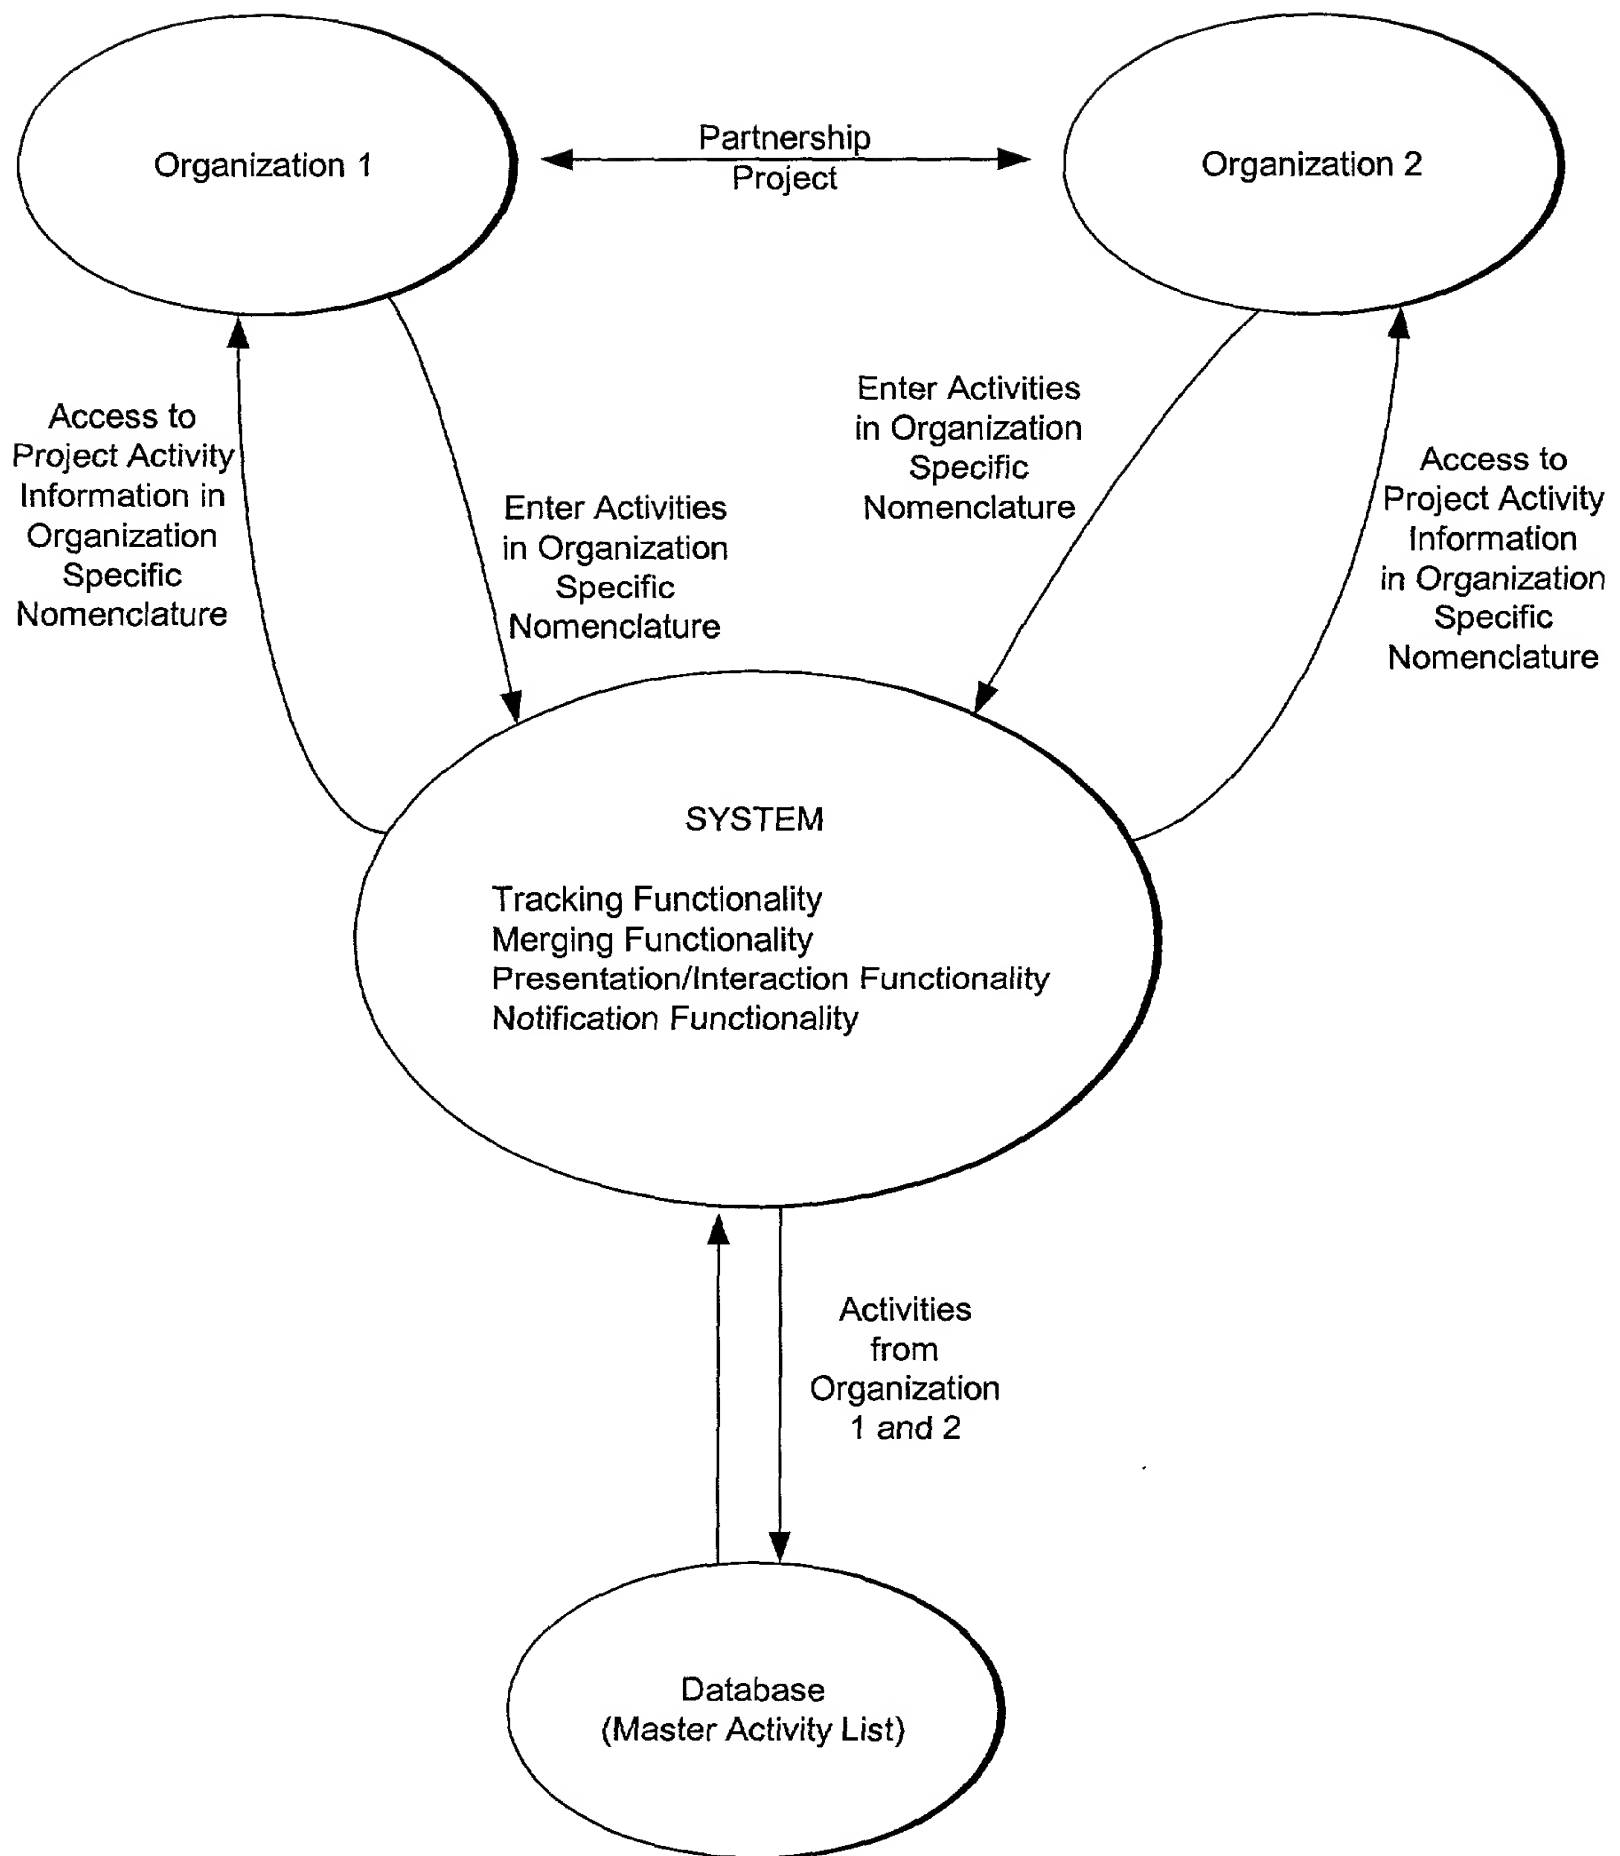


Fig. 25

0966710-092601
10860-079660

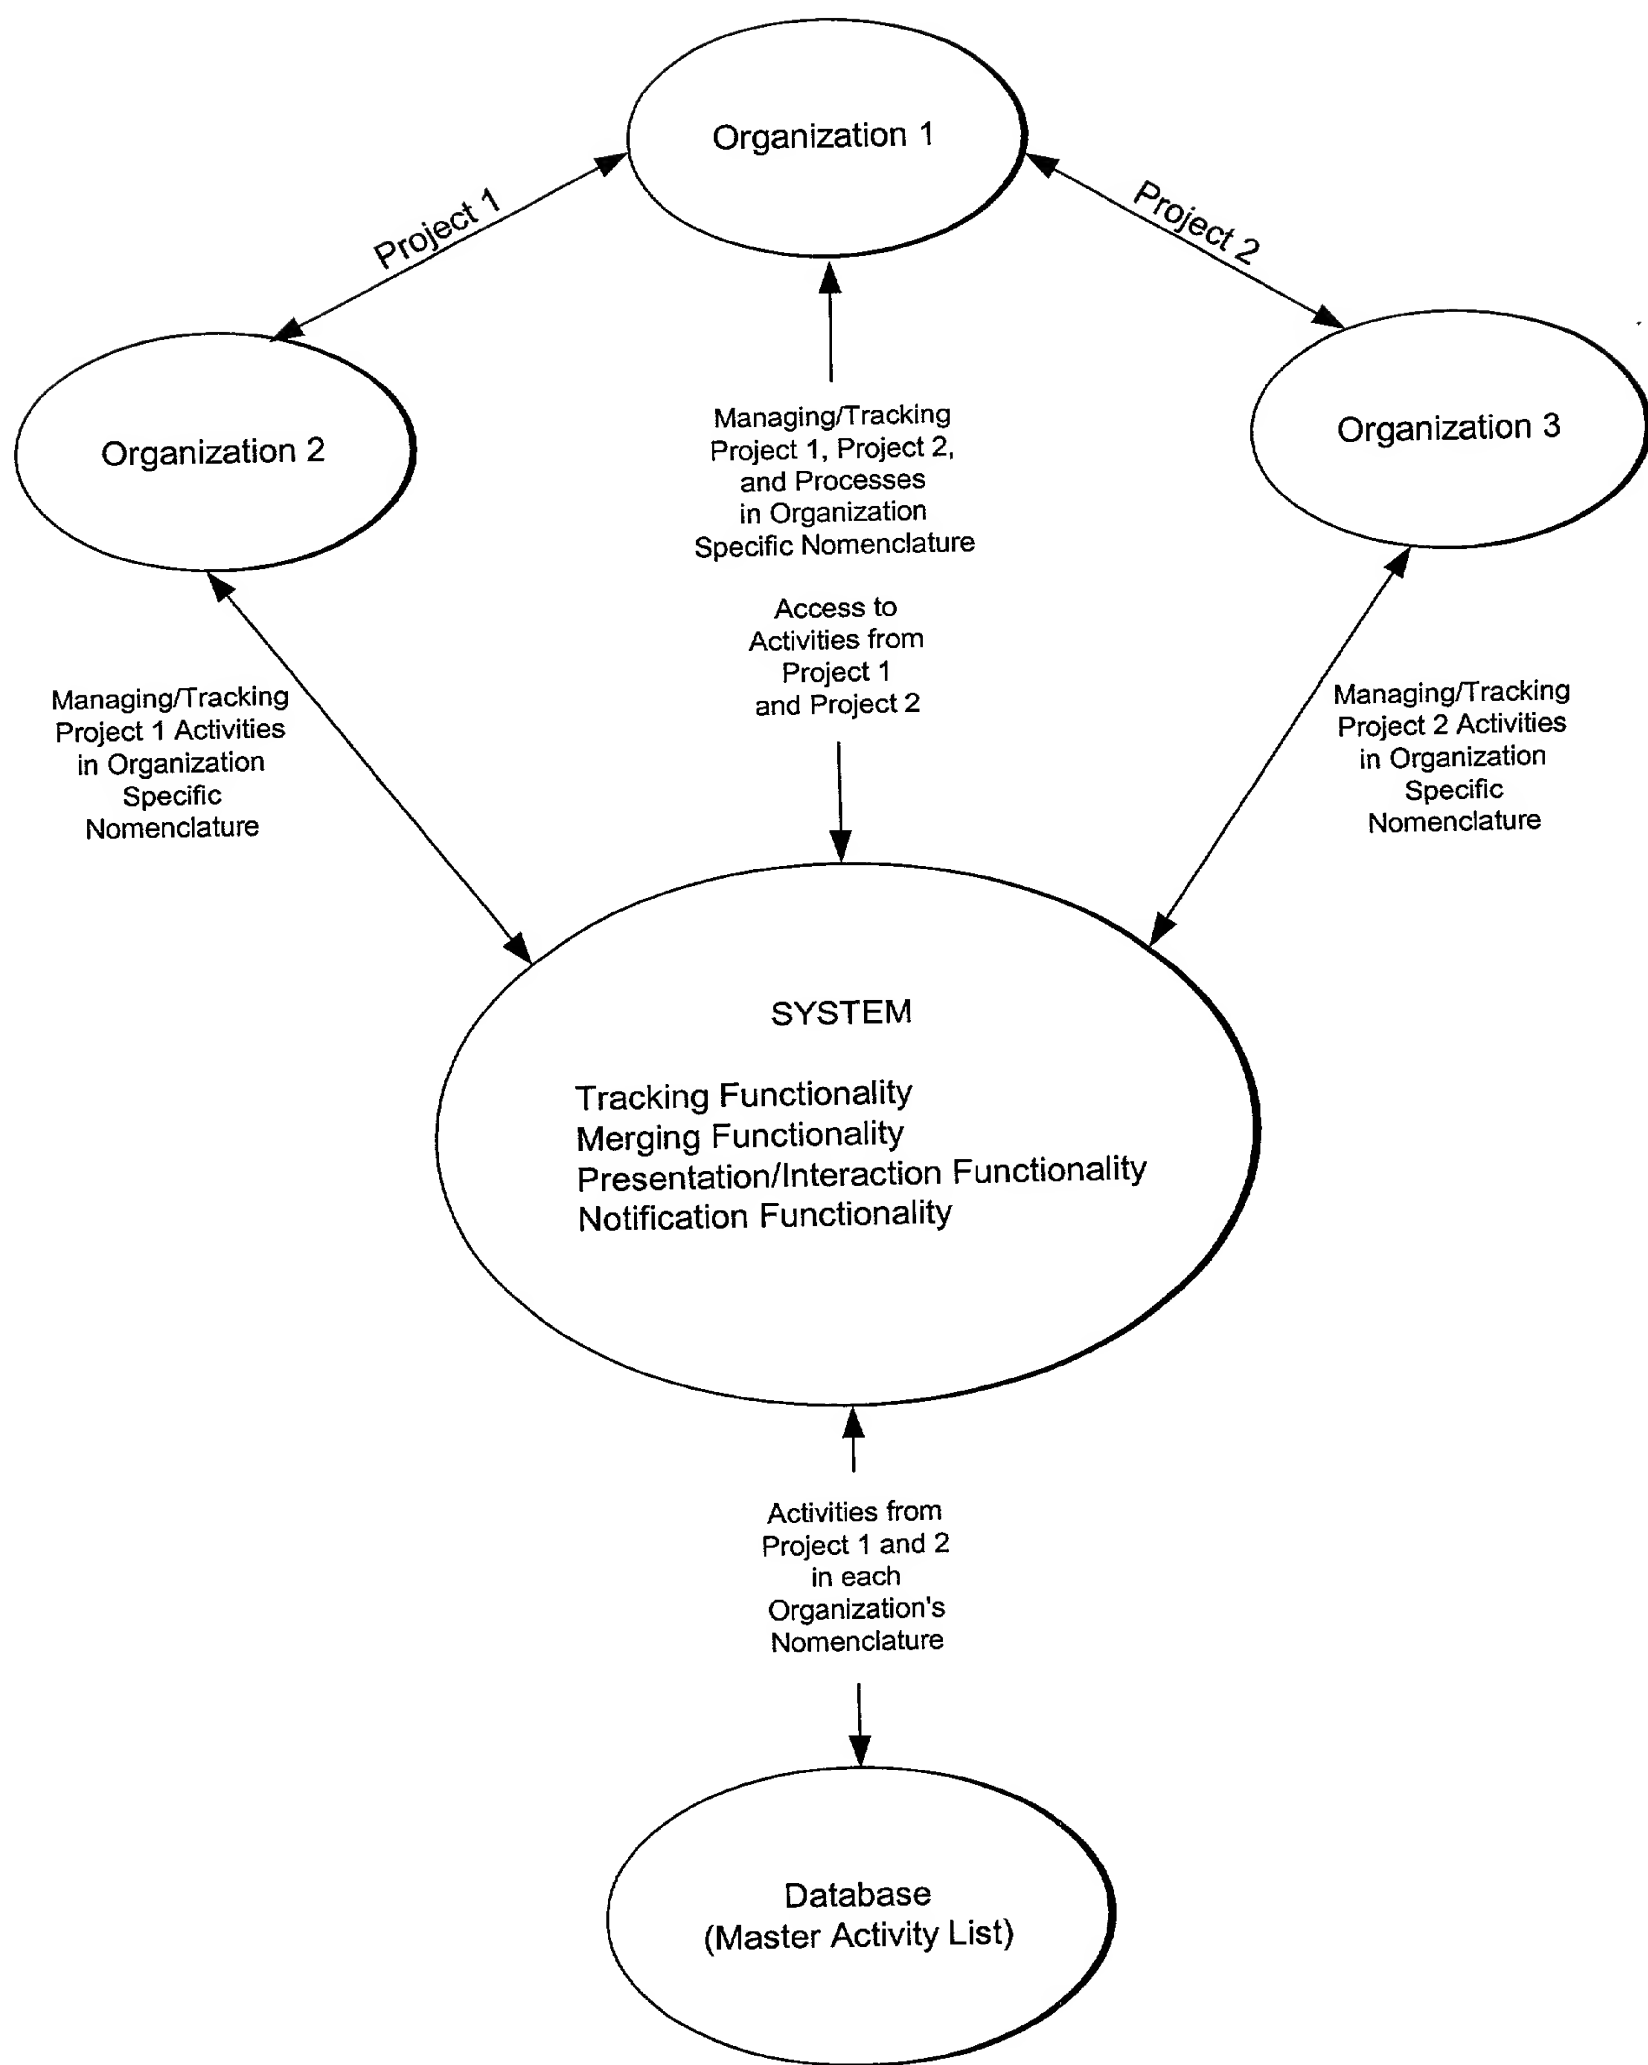


Fig. 26
